



END B
 5709 ESTERO BLVD
 26.429214°, -81.911992°
 MP: ---

END A
 5700 ESTERO BLVD
 26.429085°, -81.912109°
 MP: ---

Segment 3 Leg 2 - Lenell Rd. to Sterling Ave.
 Estero Blvd.:
 Underground work - 08/13/24 through 10/12/24
 Above ground work - 10/21/24 through 03/15/25
 Side Streets: Polygon L - M
 Underground work - 08/05/24 through 09/12/24
 Above ground work - 04/25/25 through 05/19/25

Sequence of Construction
 1. Underground Work on Estero Blvd. and Side Streets south to north (07/15/24 - 01/02/25)
 2. Above ground lighting on Estero Blvd. south to north (08/21/24 - 05/19/25)
 3. Above ground lighting on Side Streets south to north (03/26/25 - 09/12/25)

Segment 3 Leg 1 - Estrelita Dr. to Lenell Rd.
 Estero Blvd.:
 Underground work - 07/15/24 through 9/08/24
 Above ground work - 08/21/24 through 12/30/24
 Side Streets: Polygon N
 Underground work - 07/22/24 through 08/18/24
 Above ground work - 03/26/25 through 04/25/25

LEGEND

CITY	[Symbol]
COUNTY	[Symbol]
DOT	[Symbol]
RAILROADS	[Symbol]
TOWNSHIPS	[Symbol]
USACE CANAL	[Symbol]
DEP CANAL	[Symbol]

START B
 8387 ESTERO BLVD
 26.404938°, -81.885007°
 MP: ---

START A
 8352 ESTERO BLVD
 26.404719°, -81.885467°
 MP: ---

PREPARED BY:
ASPIRE COMMUNICATIONS

PREPARED FOR:
NEXTcity NETWORKS
 A NEXTERA ENERGY COMPANY

PROJECT DESCRIPTION:
 INSTALLATION OF UNDERGROUND FIBER OPTIC CABLE IN CONDUIT VIA DIRECTION BORE AND/OR TRENCHING AND A PROPOSED BRIDGE ATTACHMENT WITH THE PUBLIC RIGHT OF WAY AND/OR UTILITY EASEMENTS.


AUTHORITY HAVING JURISDICTION:
 TOWN OF FORT MYERS BEACH

PROJECT CONTACTS:
 NEXTCITY NETWORKS PM:
 ERIK DEL FORN
 954-815-8384
 erik.delforn@fpl.com
 ENGINEERING VENDOR PM:
 GUSTAVO GORDILLO
 (561) 436-8001
 ggordillo@draftelplus.com

ENGINEER SEAL:

SITE NAME:
 ESTERO ISLAND - SEG 1
SITE TRACKER ID:
 -
SITE ADDRESS:
 102 ESTERO BLVD
 FORT MYERS BEACH, FL, 33931

PREPARED BY: ASPIRE
 APPROVED BY: DT+
 DRAWN BY: DT+
 WO #: -
 DATE: 01/04/24
SHEET NAME & NUMBER:
 T-05

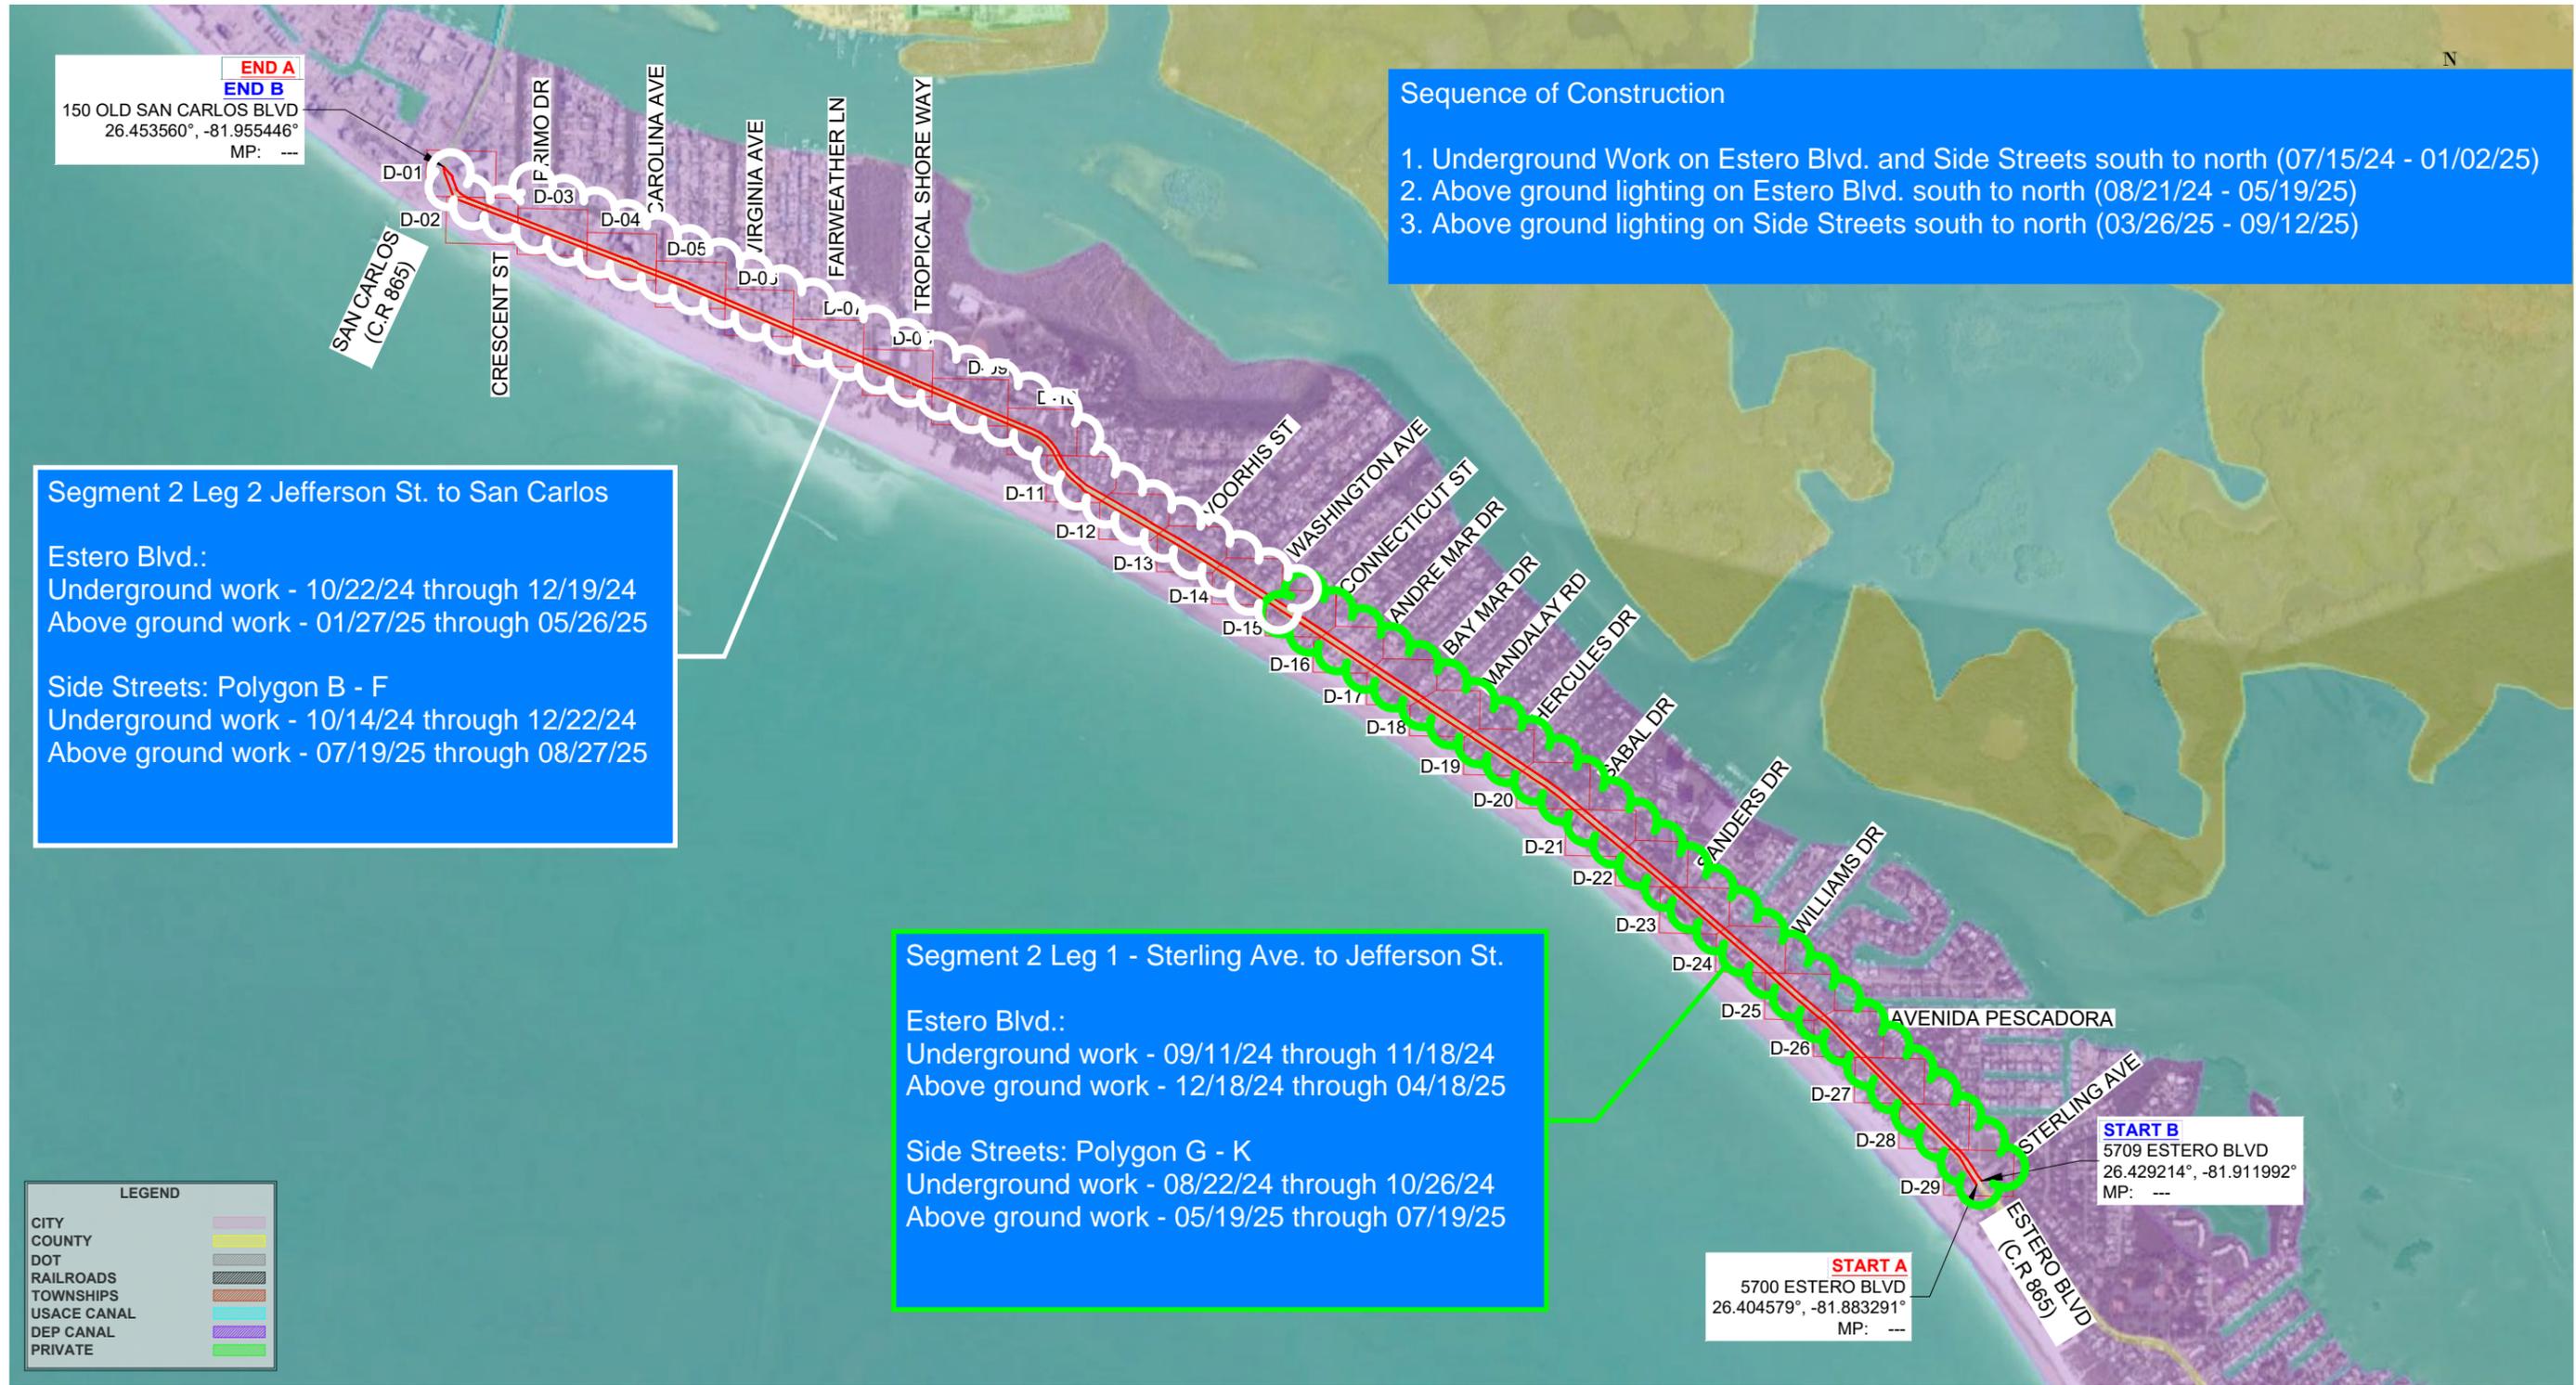

Sequence of Construction

1. Underground Work on Estero Blvd. and Side Streets south to north (07/15/24 - 01/02/25)
2. Above ground lighting on Estero Blvd. south to north (08/21/24 - 05/19/25)
3. Above ground lighting on Side Streets south to north (03/26/25 - 09/12/25)

Segment 2 Leg 2 Jefferson St. to San Carlos

Estero Blvd.:
 Underground work - 10/22/24 through 12/19/24
 Above ground work - 01/27/25 through 05/26/25

Side Streets: Polygon B - F
 Underground work - 10/14/24 through 12/22/24
 Above ground work - 07/19/25 through 08/27/25

Segment 2 Leg 1 - Sterling Ave. to Jefferson St.

Estero Blvd.:
 Underground work - 09/11/24 through 11/18/24
 Above ground work - 12/18/24 through 04/18/25

Side Streets: Polygon G - K
 Underground work - 08/22/24 through 10/26/24
 Above ground work - 05/19/25 through 07/19/25

LEGEND

CITY	[Pink Box]
COUNTY	[Yellow Box]
DOT	[Grey Box]
RAILROADS	[Black Box]
TOWNSHIPS	[Brown Box]
USACE CANAL	[Light Blue Box]
DEP CANAL	[Purple Box]
PRIVATE	[Green Box]

PREPARED BY:

PREPARED FOR:

PROJECT DESCRIPTION:
 INSTALLATION OF UNDERGROUND FIBER OPTIC CABLE IN CONDUIT VIA DIRECTION BORE AND/OR TRENCHING AND A PROPOSED BRIDGE ATTACHMENT WITH THE PUBLIC RIGHT OF WAY AND/OR UTILITY EASEMENTS.

AUTHORITY HAVING JURISDICTION:
 LEE COUNTY
 FDOT

PROJECT CONTACTS:

NEXTCITY NETWORKS PM:
 ERIK DEL FORN
 954-815-8384
 erik.delforn@fpl.com

ENGINEERING VENDOR PM:
 GUSTAVO GORDILLO
 (561) 436-8001
 ggordillo@draftelplus.com

ENGINEER SEAL:

SITE NAME:
 ESTERO ISLAND - SEG 2

SITE TRACKER ID:
 -

SITE ADDRESS:
 150 OLD SAN CARLOS BLVD
 FORT MYERS BEACH, FL, 33931

PREPARED BY: ASPIRE
 APPROVED BY: DT+
 DRAWN BY: DT+
 WO #: -
 DATE: 01/04/24

SHEET NAME & NUMBER:
 T-05

Sequence of Construction

1. Underground Work on Estero Blvd. and Side Streets south to north (07/15/24 - 01/02/25)
2. Above ground lighting on Estero Blvd. south to north (08/21/24 - 05/19/25)
3. Above ground lighting on Side Streets south to north (03/26/25 - 09/12/25)

END A
 102 ESTERO BLVD
 26.462390°, -81.966098°
 MP: ---

END B
 275/322 ESTERO BLVD
 26.462340°, -81.965918°
 MP: ---

Segment 1 Leg 1

Estero Blvd.:
 Underground work - 11/20/24 through 12/26/24
 Above ground work - 03/06/25 through 05/13/25

Side Streets: Polygon A
 Underground work - 12/05/24 through 12/26/24
 Above ground work - 08/27/25 through 09/12/25

Segment 1 Leg 2

Estero Blvd.:
 Underground work - 11/28/24 through 01/02/25
 Above ground work - 03/17/25 through 05/19/25

Side Streets: Polygon A
 Underground work - 12/05/24 through 12/26/24
 Above ground work - 08/27/25 through 09/12/25

START B
 150 OLD SAN CARLOS BLVD
 26.453560°, -81.955446°
 MP: ---

START A
 1028 FIFTH ST
 26.453339°, -81.955410°
 MP: ---

LEGEND

CITY	
COUNTY	
DOT	
RAILROADS	
TOWNSHIPS	
USACE CANAL	
DEP CANAL	
PRIVATE	



PREPARED BY:

PREPARED FOR:

PROJECT DESCRIPTION:
 INSTALLATION OF UNDERGROUND FIBER OPTIC CABLE IN CONDUIT VIA DIRECTION BORE AND/OR TRENCHING AND A PROPOSED BRIDGE ATTACHMENT WITH THE PUBLIC RIGHT OF WAY AND/OR UTILITY EASEMENTS.

AUTHORITY HAVING JURISDICTION:
 TOWN OF FORT MYERS BEACH

PROJECT CONTACTS:

NEXTCITY NETWORKS PM:
 ERIK DEL FORN
 954-815-8384
 erik.delforn@fpl.com

ENGINEERING VENDOR PM:
 GUSTAVO GORDILLO
 (561) 436-8001
 ggordillo@draftelplus.com

ENGINEER SEAL:

SITE NAME:
 ESTERO ISLAND - SEG 1

SITE TRACKER ID:
 -

SITE ADDRESS:
 102 ESTERO BLVD
 FORT MYERS BEACH, FL, 33931

PREPARED BY: ASPIRE
 APPROVED BY: DT+
 DRAWN BY: DT+
 WO #: -
 DATE: 01/04/24

SHEET NAME & NUMBER:
 T-05
